




Please sketch a mud map of the debilitated area, or attach relevant map/s and photos. Please include names of waterways (if applicable) and a rough scale & orientation.

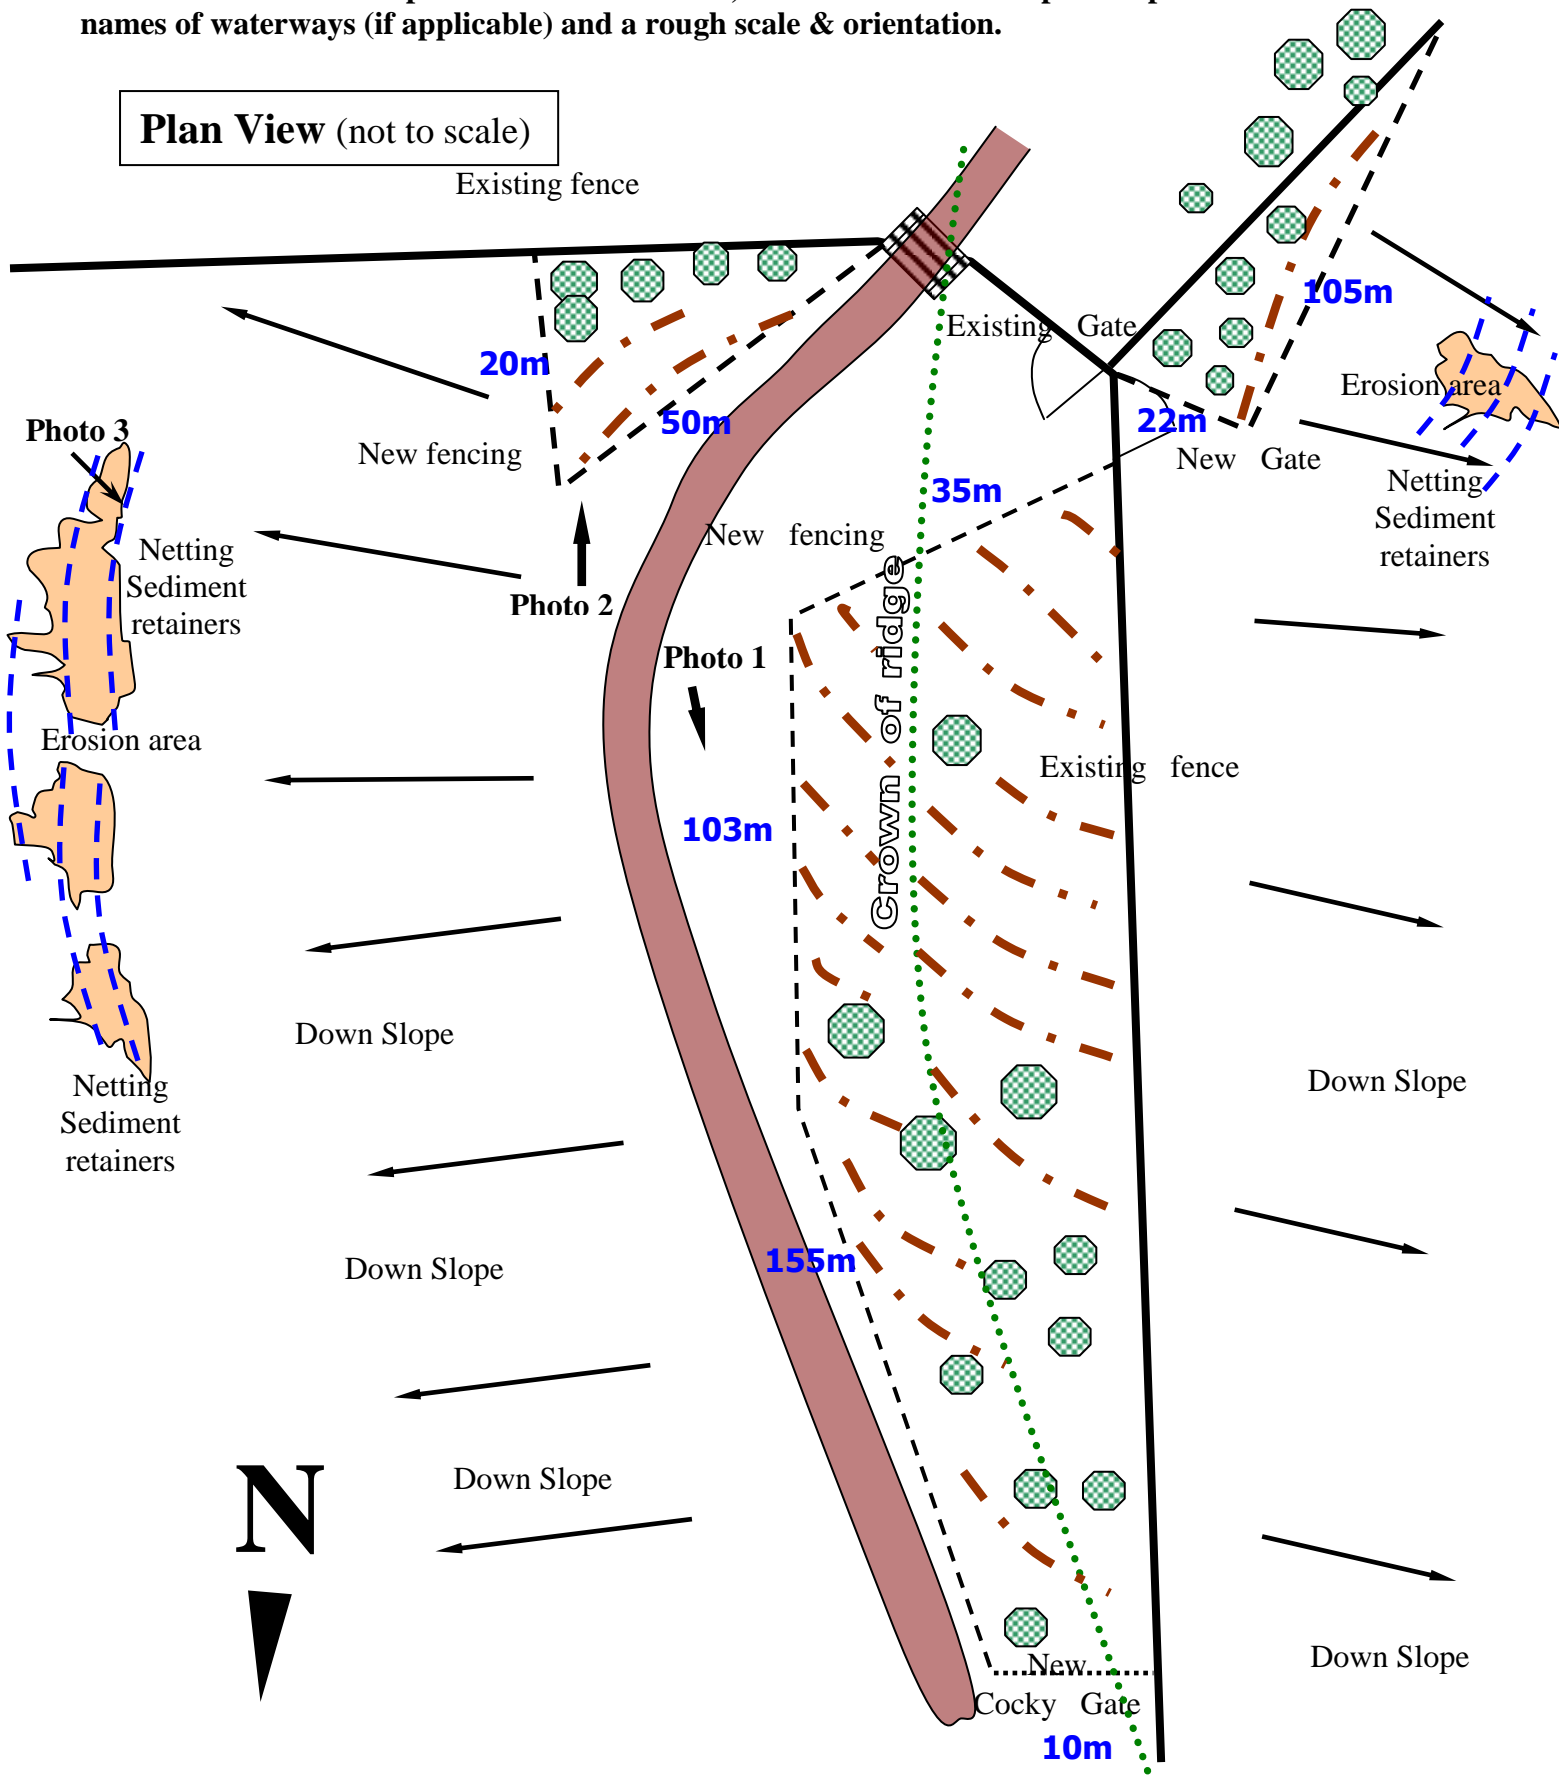

Benchmark Reference No. (group to complete): ...07-0001 T-kn-E..... Note number of pages ( / ).

Corrowong Wallendibby Landcare Group (incorporating the Tombong catchment area)

# Proposed Landcare Rehabilitation

Benchmark Reference No. (group to complete): ...07-0001 T-kn-E...

**Would you like a site visit from the Coordinator or technical expert to discuss your issue?**.....

Contact person: ... *Rowan Wright*..... Telephone: ...*64588134*..... E-mail: ...*knock@rowansweb.com*..

**Proposed Rehabilitation:** (please also complete the summary table on the following page):

...*Deep ripping in Contours, Mounding in Contours, weed control, and fencing out stock from the area.*

*One side of the area has an existing fence.*

*The whole area to be fenced off (500 m) using ring lock & one top wire or alternatively a plain 7 wire fence , Timber strainers & stays and steel posts at 4 metre spacings*

*Planting of native vegetation including both trees and shrubs in alternating rows @ 3 m spacings.*

*The sheet erosion areas are to be broken up with deep ripping and formed to the surrounding land form.*

*Additional humus material shall be added to the erosion area and where a slope of more than 4:1 exists mesh retaining barriers shall be installed.*

.....  
.....  
.....

Estimated Labour required: ..... *one person* ..... Hours of Labour: ...*43 hours labour*

Description of Machinery required: ... *Tractor, ripper, earth moulder & spray equipment. All on farm.*

.....  
.....  
.....

Description of Materials required: ... *Strainers and stays, one latch post, steel posts, 500 metres of ring lock & 500 m of HT wire Alternatively 3500m of HT wire for a 7 wire fence . 200m of netting for erosion retaining fences. Native trees & shrubs.*

.....  
.....

**Attach and number additional pages as required**..... Note number of pages ( / ).  
Corrowong Wallendibby Landcare Group (incorporating the Tombong catchment area)

**Table 1. Summary of Activities/Materials/Labour Required for Rehabilitation**

Benchmark Reference No. (group to complete): ...07-0001 T-kn-E...

<b>Activity</b> <i>(Fencing, earth moving, tree planting, weed or feral animal control etc.)</i>	<b>Description of materials/costs</b> <i>(e.g. meters of fencing, no. trees/hourly rate)</i>	<b>Machinery required</b> <i>(and estimated no. hrs)</i>	<b>Estimated labour required (hrs)</b>	<b>Cost</b> <i>(group to audit)</i>
<i>Earth preparation</i>	<i>Tractor@\$30/hour, plough @ \$3.48/hour, Moulder @ \$2.10/hour</i>	<i>115 HP Tractor (15 hours), with ripping(4 hours) , ploughing(7 hours) &amp; moulding implements(4 hours).</i>	<i>15 @ \$ 30/hour</i>	<i>\$450+ \$24+ \$10+\$450 = \$934</i>
<i>Fencing</i>	<i>125 star posts, 500m ring lock, 500m HT wire, 9 strainer posts, 10 stays. Calculated @ \$2.50/metre. Foot netting, Tractor @ \$30/hour for 3 hours</i>	<i>115 HP Tractor (3 hours), Post hole digger, hand tools.</i>	<i>14 @ \$30/h</i>	<i>\$1310 + \$90+ \$420 = \$1820</i>
<i>Weed spraying</i>	<i>Herbicide + machinery costs @\$17/hour</i>	<i>4 wheel drive vehicle &amp; boom spray</i>	<i>4 @ \$30/h</i>	<i>\$68+ \$120 = \$180</i>
<i>Tree planting</i>	<i>300 trees &amp; shrubs @ \$1.5/plant</i>	<i>None</i>	<i>10 @ \$30/h</i>	<i>\$450+ \$300 = \$758</i>
<div style="border: 1px solid black; padding: 5px;"> <p><b>Increased material costs</b>                      Star posts now \$4.70, Foot netting - \$90.00, Ring-Lock - \$242.00, strainer posts - \$30.80 &amp; stays – 18.70, HT Wire - \$</p> <p><b>Summing up</b>                      2 x 90 = \$180, 9 x 30.80 = \$277.20, 1 x \$168,30, 4 x \$61 = \$244.</p> <p><b>Sub total</b>                      Fencing = \$869,50                      Trees = \$450</p> <p><b>TOTAL</b>  <b>\$1319.50</b></p> </div>				
	<b>Materials</b>	<b>Machinery costs</b>	<b>Labour</b>	
<b>Sub totals</b>	<i>\$1760</i>	<i>\$642</i>	<i>\$1290</i>	<i>\$3692</i>
		<b>15% administration</b>	<i>\$554</i>	
			<b>Total</b>	<i>\$4246</i>

